



PVHS Fields, Fieldhouse, and Bleachers Project


August 2022

Work Completed Last Month

- **Upper Courts:** Installation of tennis/basketball fence posts, concrete borders, and trench drains are substantially complete.
- **Field House:** Electrical/plumbing fixtures are substantially complete. Interior paint, tile, windows, and roof are complete. Installation of toilet partition/accessories, weight room mirrors, lockers, and concession countertops will be completed this month.
- **Baseball Softball:** Fence posts and fabric for softball/baseball fields are substantially complete. Asphalt work, bleachers, and synthetic turf for baseball/softball fields are ongoing.
- **Main Stadium/Bleachers:** Stadium lights and scoreboard are operational. This phase was occupied by the District as of 8/8/22.

Work to be Completed This Month

- **Upper Courts:** Installation of valley gutters, final grading, pavement and court accessories will be substantially complete by end of the month.
- **Field House:** Installation of gates and fences, asphalt, and flatwork at the field office exterior is ongoing.
- **Baseball Softball:** Installation of synthetic turf ongoing. Landscape work to begin soon.

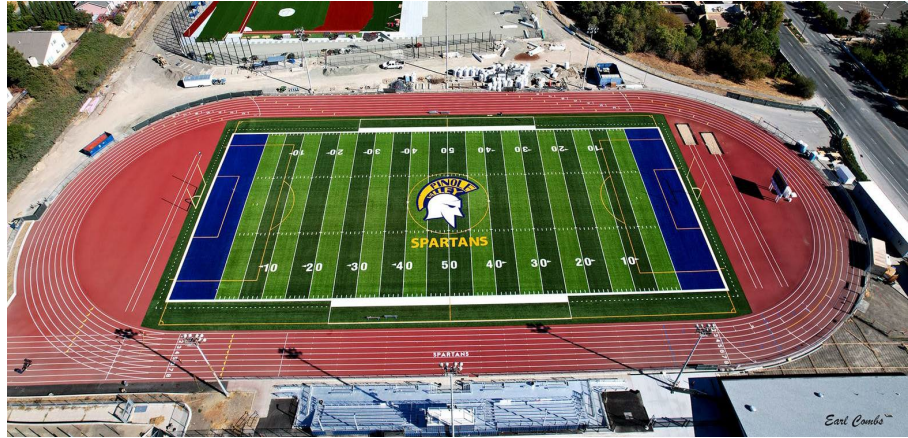

Project Facts

- **Project Scope:** New fieldhouse, tennis courts, basketball courts, baseball and softball fields, track and field resurfacing, new home and away bleachers, new press box.
- **Total Square Feet:** 464,000 SF
- **Architect:** PBK/ WLC Architects
- **Anticipated Completion:** Fall 2022

Project Website:

<https://www.wccusd.net/Page/15634>



Contact Information

Contractor: CWS Construction
415 599-5585

Construction Manager:
RGM Kramer Inc
925 671-7717

To subscribe to this monthly newsletter or ask a project questions, please email:
askfacilities@wccusd.net

