

Facilities

Annual Update of the Facilities Master Plan

Non-Bond Summer Projects

July 2023

El Cerrito

Kensington

Indian

Rock Park



Agenda

Annual Update of the Facilities Master Plan

- Projects Finishing Design and In Construction
- Next Phase of Master Plan Project Implementation

Summer Projects Update

Fund 21: Bond Fund

Measure D2010 & E2012:

Legacy Projects: commenced prior to 2016 Facilities Master Plan (FMP)


2016 FMP Projects: Critical Needs & Campus Replacement

Measure R2020: KHS Fields Project & Master Planning for KHS & RHS

2016 Facilities Master Plan Implementation

Board Approved 2016 Facilities Master Plan Implementation Project Status

Board Approved 20 School	Project Type	FMP 2016		rrent Budget	Status
Ed Specs & School Size	, ,,	\$	200,000	\$ 200,000	Completed
Cameron School	Critical Needs	\$	1,300,000	\$ 3,500,000	Construction
Chavez Elementary School	Critical Needs	\$	600,000	\$ 72,847	Completed
Collin Elementary School	Critical Needs	\$	3,500,000	\$ 7,300,000	Construction
B.R.Soskin Middle School	Critical Needs	\$	3,100,000	\$ 5,169,597	Completed
Fairmont Elementary School	Critical Needs	\$	3,000,000	\$ 3,000,000	Closeout
Grant Elementary School	Critical Needs	\$	900,000	\$ 211,467	Completed
Harmon Knolls	Critical Needs	\$	200,000	\$ 406,946	Completed
Harmon Knolls	Soils Testing	\$	100,000	\$ 41,489	Completed
Hercules Middle School**	Critical Needs	\$	7,500,000	\$ 10,000,000	Construction
Hercules High School**	Critical Needs	\$	7,200,000	\$ 9,700,000	Construction
Highland Elementary School	Critical Needs	\$	800,000	\$ 800,000	Planning/Design
Kennedy High School	Critical Needs	\$	12,200,000	\$ 12,200,000	Planning/Design
Lake Elementary School	Critical Needs	\$	-	\$ 147,501	Completed
Lake Elementary School	RS Replacement	\$	66,100,000	\$ 65,600,000	Construction
M Obama Elementary School*	RS Replacement	\$	40,300,000	\$ 40,300,000	Closeout
Ohlone Elementary School	Critical Needs	\$	800,000	\$ 623,885	Completed
Olinda Elementary School	Critical Needs	\$	1,000,000	\$ 793,247	Completed
Richmond High School	Critical Needs	\$	15,100,000	\$ 21,000,000	Closeout
Riverside Elementary School	Critical Needs	\$	6,900,000	\$ 6,900,000	Construction
Shannon Elementary School	Critical Needs	\$	7,100,000	\$ 9,300,000	Planning/Design
Stege Elementary School	Critical Needs	\$	2,900,000	\$ 2,900,000	Planning/Design
Valley View Elementary School	Critical Needs	\$	1,000,000	\$ 1,091,447	Completed
TOTAL IMPLEMENTATION PLAN MODEL 1		\$	181,800,000	\$ 201,258,425	



State Facilities Funding Updates

\$221,620,188 School Facility Program Funding Received to Date

\$14,186,087 State Facility Grants received in 2022

Future Anticipated State Funding \$5,089,995

School	Funding	OPSC Status	SAB Approval	Fund Release	Amount
Michelle Obama ES	Modernization	On Acknowledged List	TBD	TBD	\$3,844,145
Richmond HS	Modernization	On Acknowledged List	TBD	TBD	\$1,245,850

Future Application Submissions

- Hercules MS / HS Critical Needs Project (CR Replacement Mod)
- Cameron Critical Needs Project (HVAC Mod)
- Collins ES Critical Needs Project (HVAC Mod)
- Shannon ES Critical Needs Project (MPR/CR Replacement Mod)
- Lake ES Modernization (Mod)

Note: OPSC (Office of Public School Construction) Submitted Applications amount and fund release is subject to revision.

Updating the Facilities Master Plan:

Projects In Design and Under Construction


Project Facts: Scope: Full rebuild of the campus

Status: Under Construction with final completion planned for Fall of 2025

Project Budget: 65.6 Million

Design Build Team: Alten Construction


Lake ES - Rebuild

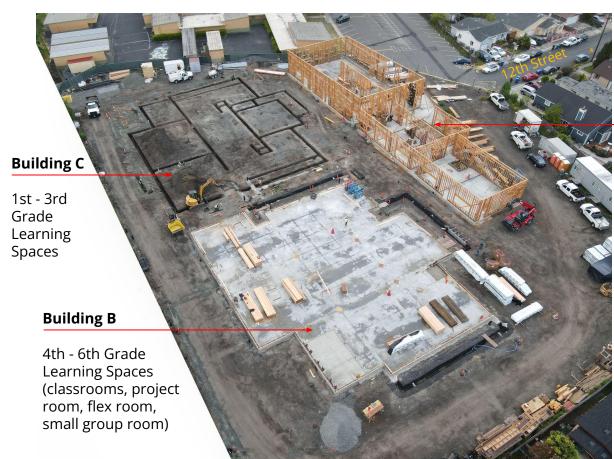

Building A

Front Door, Admin, Librar Community Room, Staff Room, Learning Center

Lake Elementary School - Rebuild



Phase 1A

1st – 6th Learning Areas, Office, Library

Phase 1B

Multi Purpose Room, Kindergarten Building/Playground



Lake Elementary School - Rebuild



Building A - Utility Rough In



Building B - Wall Framing **Building C** - Building Pad

Project Facts: Scope:

New play structures, paving improvements, new garden

Status: Soil stabilization project is complete, the playground restoration anticipated completion Fall 2023


Project Budget: \$6.9M

Architect: SVA

Contractor: ERA

Riverside ES - Critical Needs Project

Kinder Structure

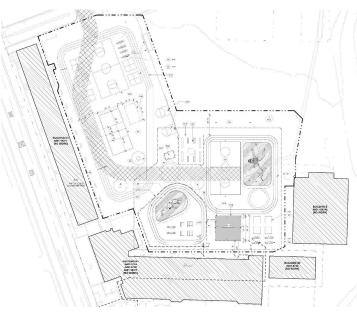



Primary Structure



Project Facts: Scope:

New grandstands and pressbox, replacing turf and track surfaces, additional pedestrian lighting

Status: Completed in June 2023

Project Budget: \$6.6M

Architect: HMC

Contractor: BHM

Kennedy HS- Field and Bleacher Project







Project Under Construction







Collins Elementary – Critical Needs

Scope: New HVAC system and associated electrical and accessibility upgrades

Project Budget: 7.3 Million

Architect: PBK

Project

Contractor: Alten

Timeline Project Facts

Construction is underway

- Interior classroom work is scheduled to be completed over the summer
- Electrical equipment delivery schedule will delay turn over to the new heating and air condition system until January 2024

Cameron – Critical Needs Project

Scope: New HVAC system and associated electrical and accessibility upgrades, replacement of the hallway flooring

Project Budget: 3.5 Million

Architect: PBK

Contractor: Alten

• Construction is underway with a temporary power solution that will allow the new heating and air conditioning system to be operational by the end of summer

Project Facts:

Scope: Replace portables and build modern science building shared by Hercules Middle and High School

Status: Completion anticipated for Fall 2024

Project Budget: \$19.7M

Architect: DSK

Contractor: Soltek

Pacific

Hercules Middle and High School -Critical Needs Project







Project Facts:

Scope: Replace the portable multipurpose room with a new permanent building.

Status: Completion anticipated for Winter 2024

Project Budget: \$9.3M

Architect: H+A

Contractor: TBD


Shannon Elementary School - Critical Needs Project





Next Phase of 2016 Master Plan Projects





Architect: HKIT

FMP Scope of Work	Timeline
Highland Elementary – Critical Needs Project Scope: Replacement of the sanitary sewer line was completed. A continuation of that project updating the restroom facilities. Project Budget: \$800,000 Architect: Arcadis	 The design is currently being reviewed by the Division of State Architect. Once approved the project will be bid. Schedule will be dependent on the school calendar and phasing
Kennedy High - Critical Needs Project Scope: Demolition of the 100 and 200 buildings and relocation to the temp campus Project Budget: \$12.2 Million	 Architect to begin design drawings for the demolition and relocation of the building system currently housed in the main office Improvements will continue to be made to the temp campus including

selective demolition of the 900

Kennedy functions in the 100 and 200 building move to the temp campus

building

Projects in Design



Project Facts	Timeline
Pinole Valley Fields Project Scope: Remaining scope includes repair to the hillside behind the tennis courts and health department approval of the concession area Project Budget: \$19.6 Million Architect: PBK Contractor: TBD	 Hillside design is being reviewed by the California Geological Survey (CGS) & DSA and upon approval will be bid Health Department review may result in additional alterations to the concession stand



Updating the Facilities Master Plan:

Next Phase of Implementation

Next Phase Measure R Master Plan Projects





FMP Scope of Work	Timeline
Kennedy High – Modernization Project	
Scope: Major architectural project to revitalize the high school campus including modernization and new construction	 Architect to complete scope and budget process Return to the Board in the fall with
Project Budget: \$1 Million scoping budget	a recommendation for the final
Architect: HKIT	project scope and phasing
Contractor: TBD	
Richmond High - Modernization Project	
Scope: Major architectural project to revitalize the high school campus including modernization and new construction	 Architect to complete scope and budget process Return to the Board in the fall with a
Project Budget: \$1 Million scoping budget	recommendation for the final project scope and phasing
Architect: DLR	F. 2122226 2 22 P. 129
Contractor: TBD	

KHS & RHS Scoping Project

Next Steps

5/7/2023 BOE Presentation


- Detailed Site investigations
- Prioritization of desired project outcomes
 - Prioritization of the project goals
 - Evaluation and assignment of the level of modernization
 - Refinement of the new construction scope

 Recommendation to the Board for a final scope, budget, and general phasing within the constraints of Measure R










Next Phase of 2016 Master Plan Projects



FMP Scope of Work	Timeline
Stege Elementary – Critical Needs Project Scope: Demolition of the office/classroom building and building and site improvements Project Budget: \$2.9 Million Architect: QKA Contractor: TBD	 Architect to complete scope and budget process Return to the Board in the fall with a recommendation for the final project scope, budget and phasing

Construction Newsletters



CONSTRUCTION NEWSLETTER



LAKE ELEMENTARY
SCHOOL REPLACEMENT
PROJECT

June 2023

Project Updates

Summer Work - Front Parking Lot

Over the summer, the parking lot connecting 11th and 12th Streets will be under construction and closed to ALL traffic. A Staff-Only parking lot will be available through the summer and during next school year.

The NEW 11th Street parking lot will reopen for families and community access by the start of

New format has great new features

- Adjusts image and text scales for viewing on different size screens
- Auto translation
- Integration into Parent Squared
- Ability to expand smaller images
- Ability to add videos



Sign Up For Newsletters

https://forms.gle/NL3B5ZBcSPZ5GZSA8



Non-Bond Funding:

Summer Project

Play Structure Projects

This Summer	Designed Projects
 Downer Kinder and Preschool Structures/Safety Surface Kensington Main Playground Safety Surface and Preschool Structure/Safety Surface Madera Kinder Structures/Safety Surface (includes blacktop resurfacing) Steward Main Playground Safety Surfaces and Kinder Structure/Safety Surface Tara Hills Kinder and Primary Structures/Safety Surface Shannon Main Playground Structure/Safety Surface 	 Washington Main Playground Structure and Safety Surface Olinda Main Playground Structure/Safety Surface Verde Main Playground Structure/Safety Surface Bayview Intermediate Playground Structure/Safety Surface

^{*}All play structure projects include accessibility improvements such as drop off improvements, ADA parking striping, restroom changes, drinking fountain replacements

Summer Projects

Exterior Painting Projects -

- Betty Reid Soskin
- Kensington
- Madera
- Mira Vista
- Cameron
- Kennedy High School Concession



De Anza HS - Turf replacement and track coating

Shannon ES - Portable Classroom Replacement

Highland ES - Electrical and Water infrastructure improvements

Korematsu MS - Gym Floor Repair

Cameron - Roof Replacement

Madera - Gutter Replacement
